ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
1		Project initialization	1 day	Sat 30 03 19	Sat 30 03 19		toàn	100%
2		**Database**	**2 days**	**Sun 31 03 19**	**Tue 02 04 19**	**1**		**100%**
3		Database construction (Entities)	2 days	Sun 31 03 19	Mon 01 04 19		toàn	100%
4		Input template data	1 day	Tue 02 04 19	Tue 02 04 19	3	toàn	100%
5		**Back-end**	**19 days**	**Tue 02 04 19**	**Sat 27 04 19**			**66%**
6		DAO	2 days	Tue 02 04 19	Wed 03 04 19	3	Việt	100%
7		Service	2 days	Thu 04 04 19	Fri 05 04 19	6	Việt	100%
8		**Controller**	**18 days**	**Wed 03 04 19**	**Sat 27 04 19**			**63%**
9		**Customer site**	**18 days**	**Wed 03 04 19**	**Sat 27 04 19**			**100%**
10		HomeController	1 day	Wed 03 04 19	Wed 03 04 19	4	toàn	100%
11		LoginController	1 day	Thu 04 04 19	Thu 04 04 19	10	toàn	100%
12		RegistrationController	1 day	Fri 05 04 19	Fri 05 04 19	11	toàn	100%
13		ProductController	2 days	Sat 06 04 19	Sun 07 04 19	12	toàn	100%
14		ProductDetailController	2 days	Mon 08 04 19	Tue 09 04 19	13	toàn	100%
15		CartController	2 days	Wed 10 04 19	Thu 11 04 19	14	toàn	100%
16		ContactController	1 day	Fri 12 04 19	Fri 12 04 19	15	toàn	100%
17		TrackOrderController	2 days	Sat 13 04 19	Sun 14 04 19	16	toàn	100%
18		IntroduceController	1 day	Mon 15 04 19	Mon 15 04 19	17	toàn	100%
19		**User site (after login)**	**8 days**	**Tue 16 04 19**	**Thu 25 04 19**			**100%**
20		UserHomeController	2 days	Tue 16 04 19	Wed 17 04 19	18	toàn	100%
21		UserEditInfomationController	2 days	Thu 18 04 19	Fri 19 04 19	20	toàn	100%
22		UserFavoriteController	2 days	Sat 20 04 19	Sun 21 04 19	21	toàn	100%
23		UserOrderHistoryController	2 days	Mon 22 04 19	Tue 23 04 19	22	toàn	100%

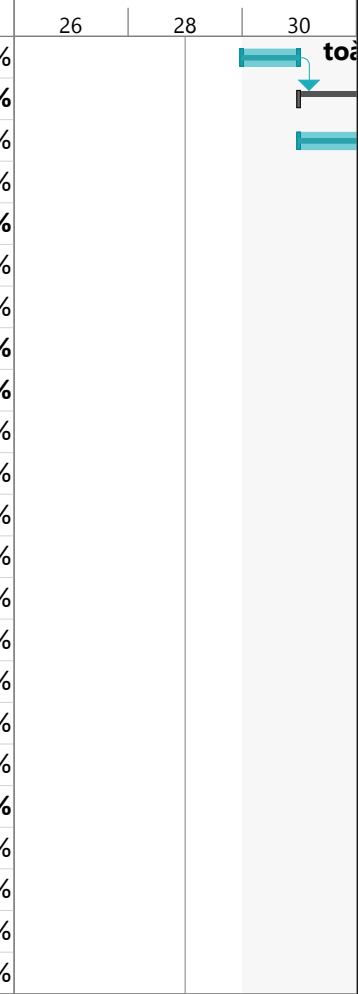

Project: Final_project
Date: Tue 16 04 19

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
24		UserOrderDetailController	2 days	Wed 24 04 19	Thu 25 04 19	23	toàn	100%
25		NewsController	1 day	Fri 26 04 19	Fri 26 04 19	24	toàn	100%
26		NewsDetailController	1 day	Sat 27 04 19	Sat 27 04 19	25	toàn	100%
27		**Admin site**	**12 days**	**Sat 06 04 19**	**Tue 23 04 19**			**11%**
28		AdminHomeController	2 days	Sat 06 04 19	Sun 07 04 19	7	Việt	0%
29		ProductManagementController	2 days	Mon 08 04 19	Tue 09 04 19	28	Việt	0%
30		CustomerOrdersController	2 days	Wed 10 04 19	Thu 11 04 19	29	Việt	0%
31		OutcomeStatisticController	2 days	Fri 12 04 19	Sat 13 04 19	30	Việt	0%
32		CategoryController	2 days	Sun 14 04 19	Mon 15 04 19	31	Việt	0%
33		AuthorController	2 days	Tue 16 04 19	Wed 17 04 19	32	Việt	0%
34		PublishingCompanyController	2 days	Thu 18 04 19	Fri 19 04 19	33	Việt	0%
35		UserController	2 days	Sat 20 04 19	Sun 21 04 19	34	Việt	0%
36		ContactMangementController	2 days	Mon 22 04 19	Tue 23 04 19	35	Việt	100%
37		**Front-end:**	**17 days?**	**Sat 30 03 19**	**Tue 23 04 19**			**67%**
38		**Customer site**	**11 days?**	**Sat 30 03 19**	**Mon 15 04 19**			**100%**
39		Home page	2 days	Sat 30 03 19	Sun 31 03 19		tiến	100%
40		Login page	1 day	Mon 01 04 19	Mon 01 04 19	39	tiến	100%
41		Registration page	2 days	Tue 02 04 19	Wed 03 04 19	40	tiến	100%
42		Cart page	2 days	Thu 04 04 19	Fri 05 04 19	41	tiến	100%
43		**User site (after login)**	**6 days**	**Sat 06 04 19**	**Mon 15 04 19**			**100%**
44		User home page	2 days	Sat 06 04 19	Sun 07 04 19	42	tiến	100%
45		User Edit Information page	2 days	Mon 08 04 19	Tue 09 04 19	44	tiến	100%
46		User Favorite List	2 days	Wed 10 04 19	Thu 11 04 19	45	tiến	100%



Project: Final_project
Date: Tue 16 04 19

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Complete
47		User Order History	2 days	Fri 12 04 19	Sat 13 04 19	46	tiến	100%
48		User Order Detail	2 days	Sun 14 04 19	Mon 15 04 19	47	tiến	100%
49		View product page	2 days	Mon 01 04 19	Tue 02 04 19	39	Đạt	100%
50		Product detail page	2 days	Wed 03 04 19	Thu 04 04 19	49	Đạt	100%
51		Contact page	2 days	Fri 05 04 19	Sat 06 04 19	50	Đạt	100%
52		Track order page	2 days	Sun 07 04 19	Mon 08 04 19	51	Đạt	100%
53		Introduce page	1 day	Tue 09 04 19	Tue 09 04 19	52	Đạt	100%
54		News page	1 day	Wed 10 04 19	Wed 10 04 19	53	Đạt	100%
55		News detail page	1 day	Thu 11 04 19	Thu 11 04 19	54	Đạt	100%
56		**Admin site**	**8 days**	**Fri 12 04 19**	**Tue 23 04 19**			**17%**
57		Admin home page	2 days	Tue 16 04 19	Wed 17 04 19	48	tiến	100%
58		Product management page	2 days	Thu 18 04 19	Fri 19 04 19	57	tiến	50%
59		Customer Orders management page	2 days	Sat 20 04 19	Sun 21 04 19	58	tiến	0%
60		Outcome Statistic page	2 days	Mon 22 04 19	Tue 23 04 19	59	tiến	0%
61		Category management page	2 days	Fri 12 04 19	Sat 13 04 19	55	Đạt	0%
62		Author management page	2 days	Sun 14 04 19	Mon 15 04 19	61	Đạt	0%
63		Publishing Company management page	2 days	Tue 16 04 19	Wed 17 04 19	62	Đạt	0%
64		User management page	2 days	Thu 18 04 19	Fri 19 04 19	63	Đạt	0%
65		Contact management page	2 days	Sat 20 04 19	Sun 21 04 19	64	Đạt	0%

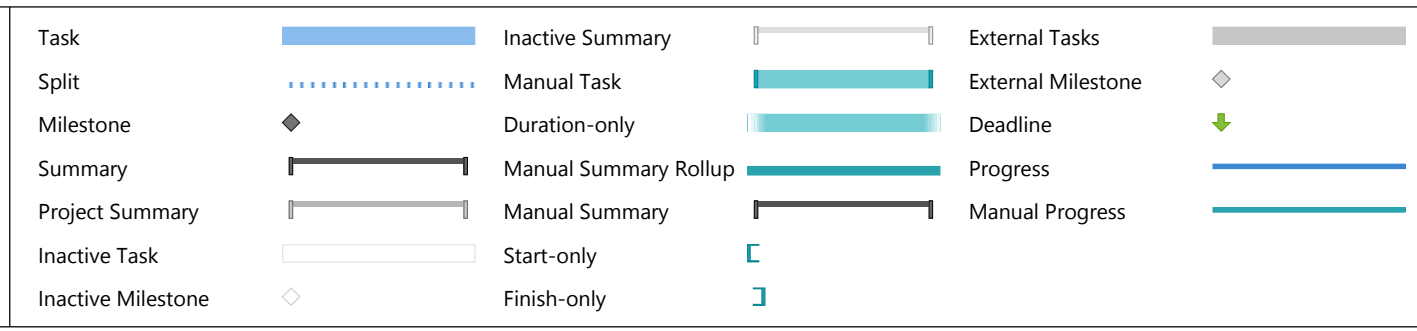

Project: Final_project
Date: Tue 16 04 19

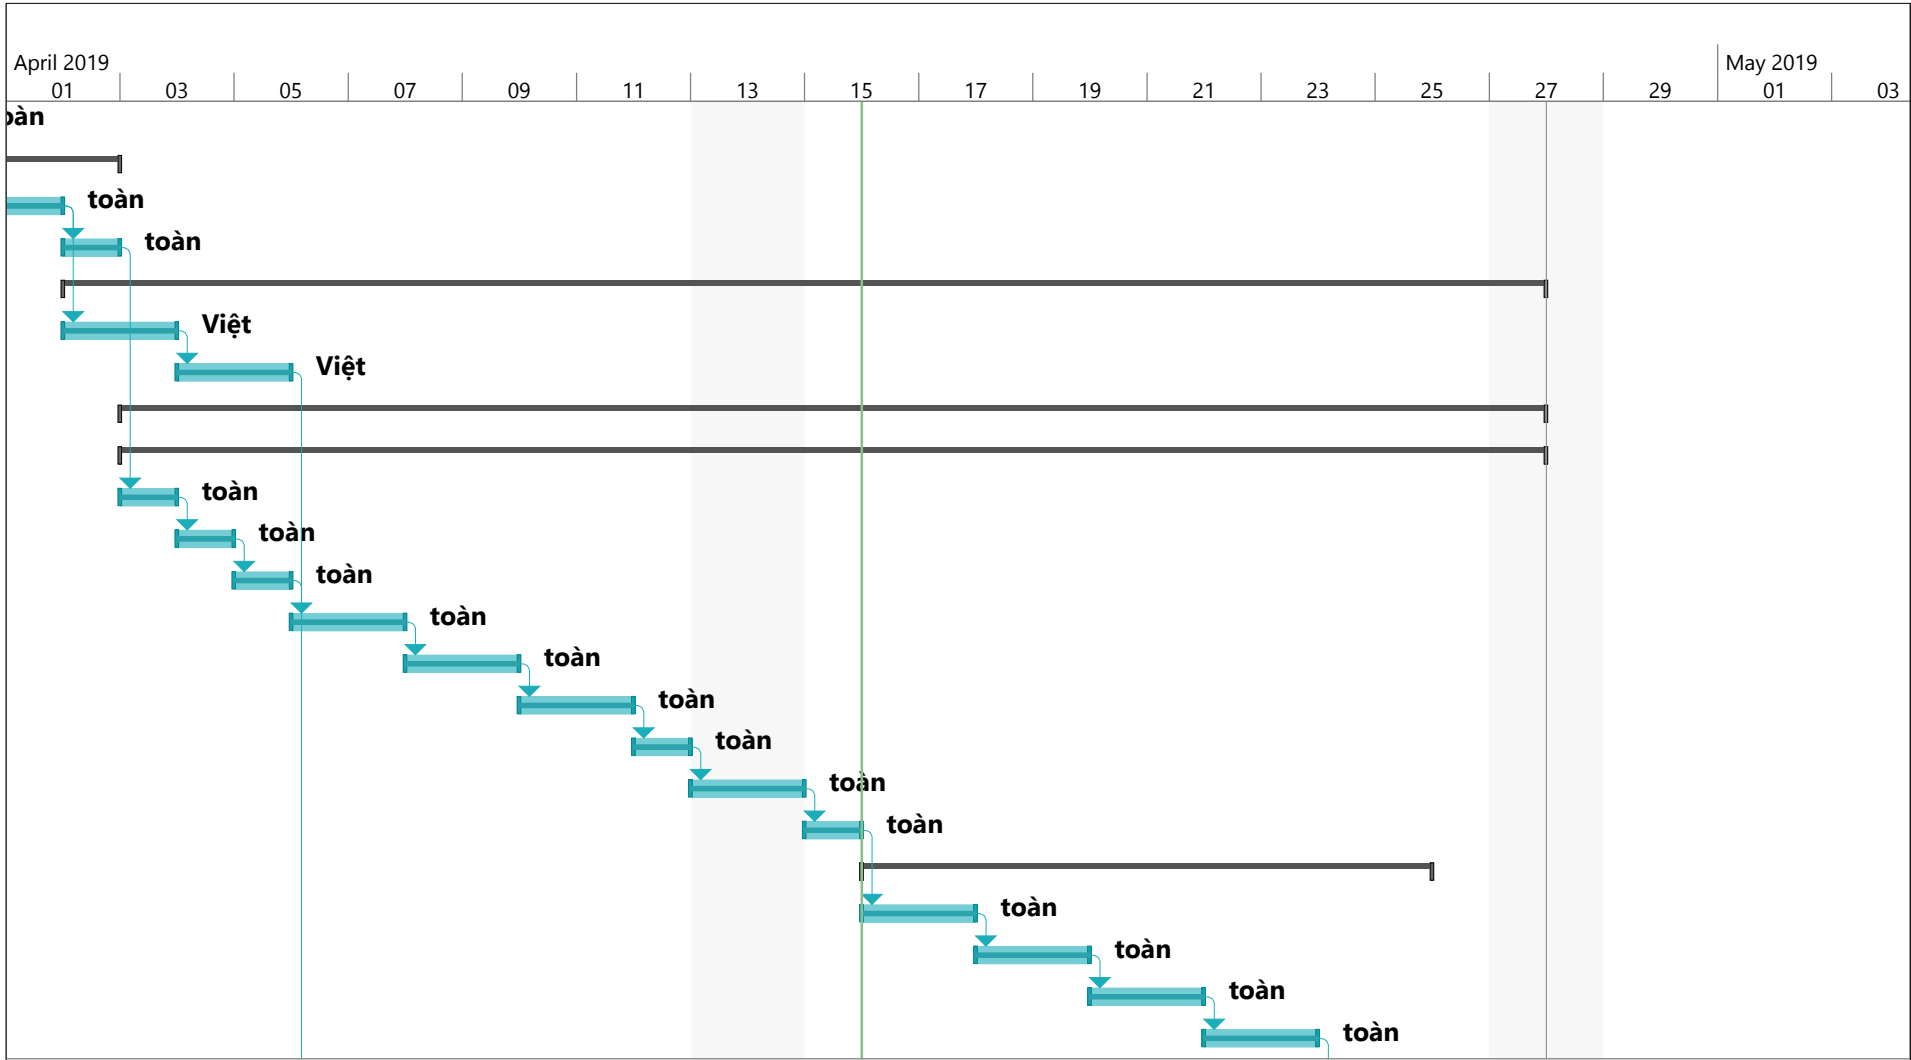

Project: Final_project
Date: Tue 16 04 19

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

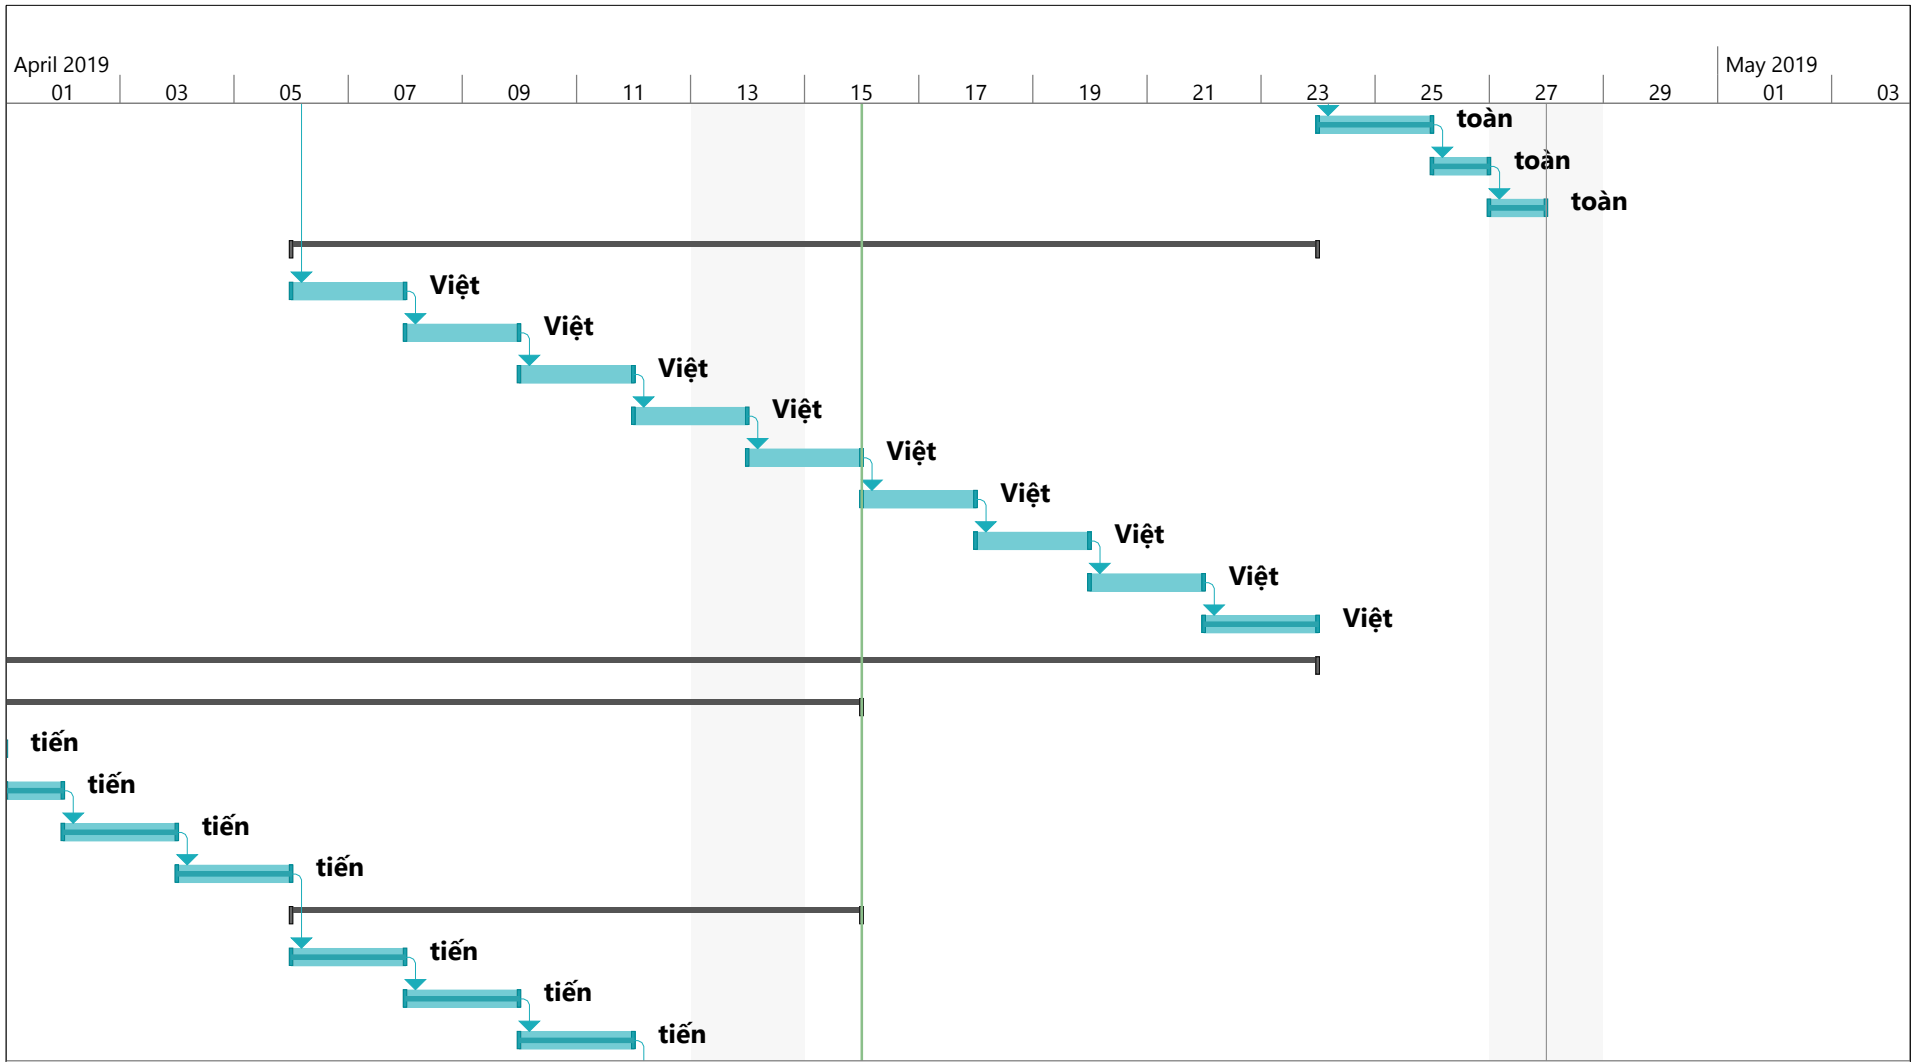

Project: Final_project
Date: Tue 16 04 19

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

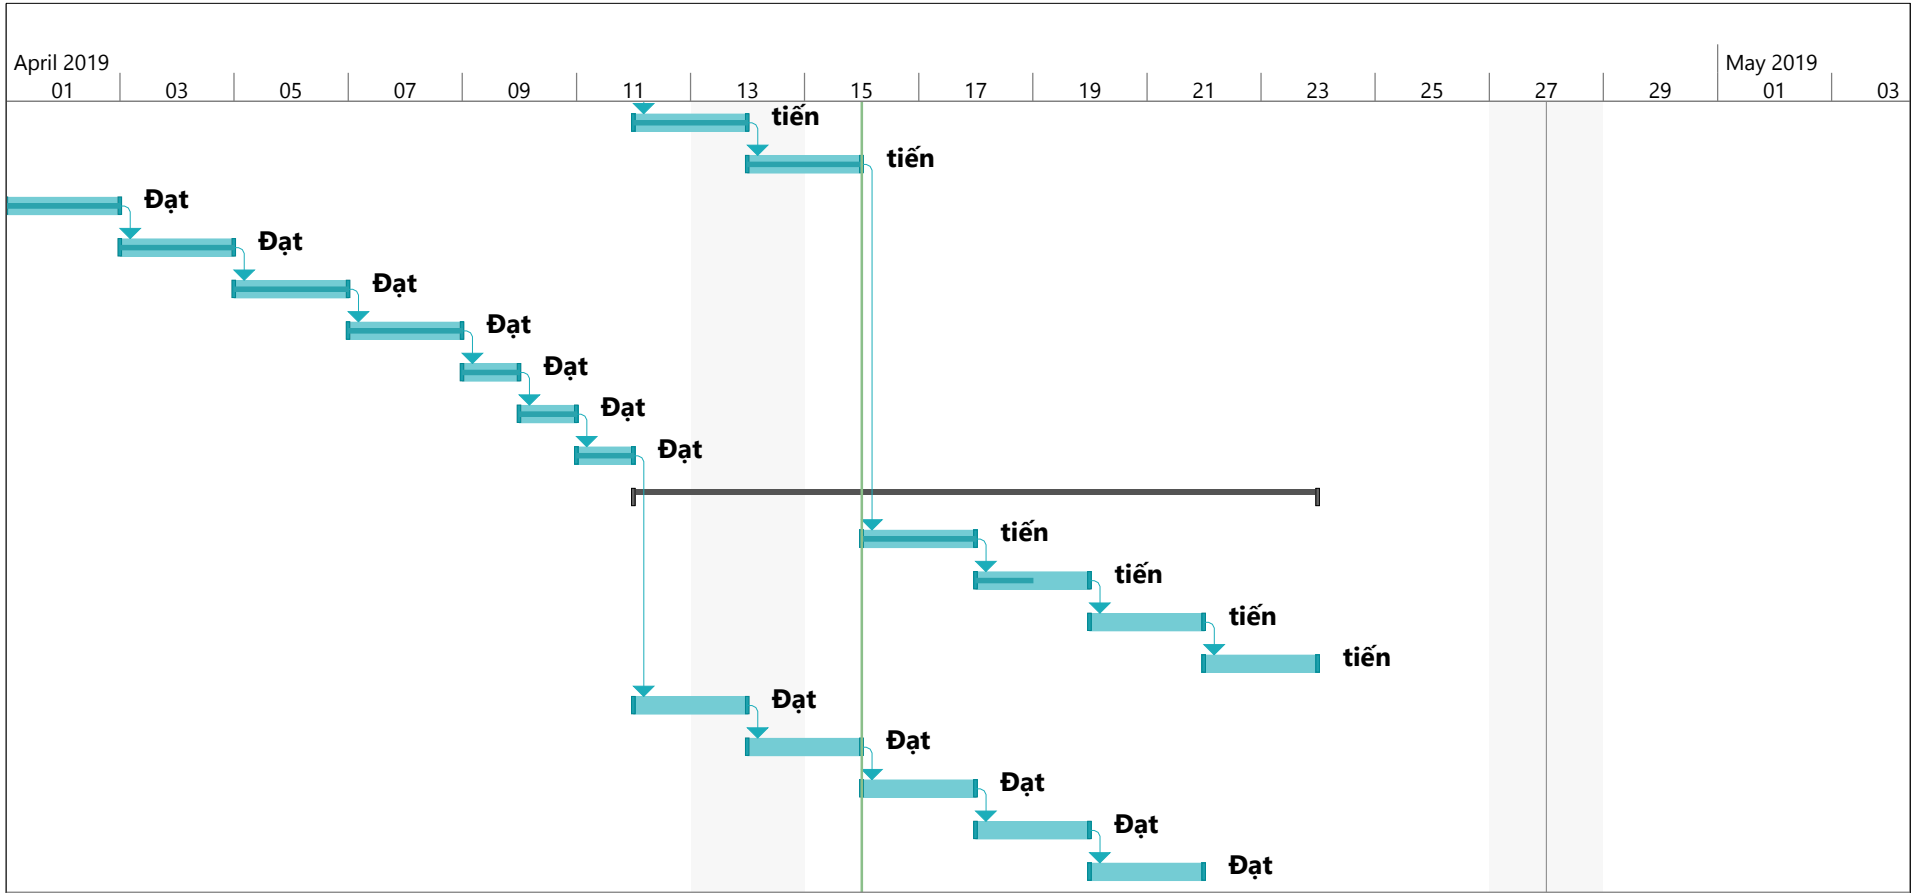

Project: Final_project
Date: Tue 16 04 19

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	
